

Facilities and Construction Group Monthly Report



**Scheduled Maintenance Projects**

Project Title	Project Status	Project Budget/PPR	Project Expenses to Date	Funding Source	Projected Const. Start/Completion	PM Comments	Issues	Photo
Exterior Lighting - Energy efficiency replacement	Design	\$40,000	N/A	MM100	5/2014 - 10/2014	Construction Drawings in process		1
Road and Parking Lot Repair	Complete	\$1,219,436	\$854,863	MM100	5/2014-8/2014	NOC and Change order #1 are being submitted for final closeout.		3
Art Room Expansion and Monument Sign	Construction	\$300,936	\$186,296	MM100	5/2014-10/2014	Construction is 60% complete awaiting cabinets. Classroom is being used by the Campus for classes.		2
Occupancy & Evacuation Signage	Construction	\$9,900	\$13,112	MM100	<b>12/2013-9/2014</b>	Final signs getting installed.		
Science Classroom Expansion	Design	\$461,700	\$0	MM100	<b>8/15-1/2016</b>	Design in progress		

**Capital Projects**

Issues

Project Photographs

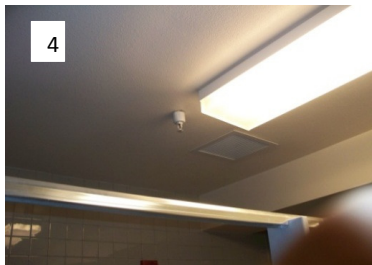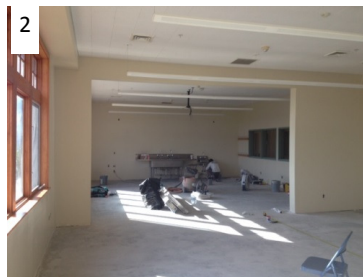

Please contact any of the following regarding questions or comments associated with this report:

Eitan Aharoni	Director of Facilities	661.336.5095	<a href="mailto:eaharoni@gafcon.com">eaharoni@gafcon.com</a>
Daniel Reed	Project Manager	661.336.5181	<a href="mailto:dareed@kccd.edu">dareed@kccd.edu</a>
Kim Crews	Administrative Assistant	661.336.5174	<a href="mailto:kcrews@kccd.edu">kcrews@kccd.edu</a>
